



**Board Report**

---

**File #:** 2016-0156, **File Type:** Oral Report / Presentation

**Agenda Number:** 20

---

**CONSTRUCTION COMMITTEE  
MARCH 17, 2016**

RECEIVE **Program Management Executive Director's oral report.**

**DISCUSSION**

RECEIVE **Program Management Executive Director's oral report.**

**ATTACHMENTS**

Attachment A - Program Management Executive Director's Report - March 2016

- **Crenshaw/LAX** - Charles Beauvoir, Deputy Executive Officer, Project Mgmt., (213)299-3095
- **Regional Connector** - Girish Roy, Deputy Executive Officer, Project Mgmt., (213)893-7119
- **Westside Purple Line Ext 1 and 2-** Dennis Mori, EO Project Mgmt., (213)922-7238
- **I-405** - Nazem Moussa, Deputy Executive Officer, Project Mgmt. (213)922-7221
- **Gerald Desmond Bridge** - Rick Clarke, Executive Director, Program Mgmt. (213)922-7557
- **Division 13** - Timothy Lindholm, EO Project Engr., (213)922-7297
- **Patsaouras Plaza Busway Station** - Timothy Lindholm, EO Project Engr., (213)922-7297
- **MRL - MOL North Hollywood Station** - Timothy Lindholm, EO Project Engr., (213)922-7297
- **Universal Pedestrian Bridge** - Timothy Lindholm, EO Project Engr., (213)922-7297
- **Presentation** - Shannon Hanley, Senior Administrative Analyst, (213)922-1350

Reviewed by: Richard Clarke, Executive Director, Program Management, (213) 922-7557

---

# Program Management -- Transit Status Report

## Significant Issues

Presented By

**Richard Clarke**

Executive Director,  
Program Management

March 2016

**Construction Committee**  
Los Angeles County Metropolitan Transportation Authority



# CRENSHAW/LAX TRANSIT PROJECT

## SIGNIFICANT HIGHLIGHTS

- Overall construction progress is 34.5% complete (excludes contractor mobilization costs). Design-builder is behind schedule but discussions continue regarding mitigation efforts.
- Continued placing invert concrete and starting wall placement at Expo/Crenshaw Station in advance of lowering tunnel boring machine into Station in March.
- Continued invert concrete placement at UG#1 in front of LAX runways.
- “Harriet” as in Harriet Tubman is name of the Tunnel Boring Machine that will excavate the tunnels.
- Southwestern Yard Design-Builder 60% design drawings under Metro review. Construction start scheduled for April 2016.



Greenline bridge falsework construction ongoing



Tunnel ventilation fabrication at Bellanca Yard

March 2016

**Construction Committee**  
Los Angeles County Metropolitan Transportation Authority



# REGIONAL CONNECTOR TRANSIT CORRIDOR

## SIGNIFICANT HIGHLIGHTS

- Overall Project Progress is 14.4%, Design Build (DB) Construction is 6.8% and DB Final Design is 88.5% complete.
- 1<sup>st</sup>/Alameda Shoofly work progressing on schedule; reopening of revenue service through Little Tokyo Station anticipated March 21.
- Piling, underground utility relocations, and demo work at 1<sup>st</sup>/Alameda continues.
- 2<sup>nd</sup>/Hope Station Yard set-up completed. Pile trenching and potholing underway; piling operations commencing for station excavation and street decking.
- Utility rearrangements and investigations along Flower Street continue.



Shoofly installation at Mangrove Yard

# WESTSIDE PURPLE LINE – SECTION 1

## SIGNIFICANT HIGHLIGHTS

The Advanced Utility Relocations (AUR) work involving three contracts is 81% complete overall.

- The Wilshire/Fairfax Advanced Utility Relocations Contract closeout has been completed; on-time and under budget.
- The Wilshire/La Cienega Advanced Utility Relocations Contractor continues with the Southern California Edison (SCE) power relocation work and the City of Beverly Hills sanitary sewer, water and storm drain relocations. This is the last AUR contract and is on schedule to complete in December 2016.



**AUR Contractor Installing SCE Electrical Vault West of La Cienega Boulevard**

Tunnels, Stations, Trackwork and Systems Design-Build Contract

- Final Design for the tunnels, three subway stations, trackwork, and systems is 75% complete overall.
- Pile installation at the Wilshire/La Brea Station is well underway in support of station excavation to begin tunneling operations.

**March 2016**

**Construction Committee**


Los Angeles County Metropolitan Transportation Authority



# WESTSIDE PURPLE LINE – SECTION 2

## SIGNIFICANT HIGHLIGHTS


- Contract C1120 – Design/Build Request for Qualifications/Request for Proposal was released on September 14, 2015.
- The firms meeting the minimum requirements as a result of the first step were announced on December 4, 2015.
- Amendment 8 to the RFP was issued on February 4, 2016.
- Price Proposals are due on May 16, 2016.
- FFGA anticipated approval August 2016.
- Contract award anticipated January 2017.

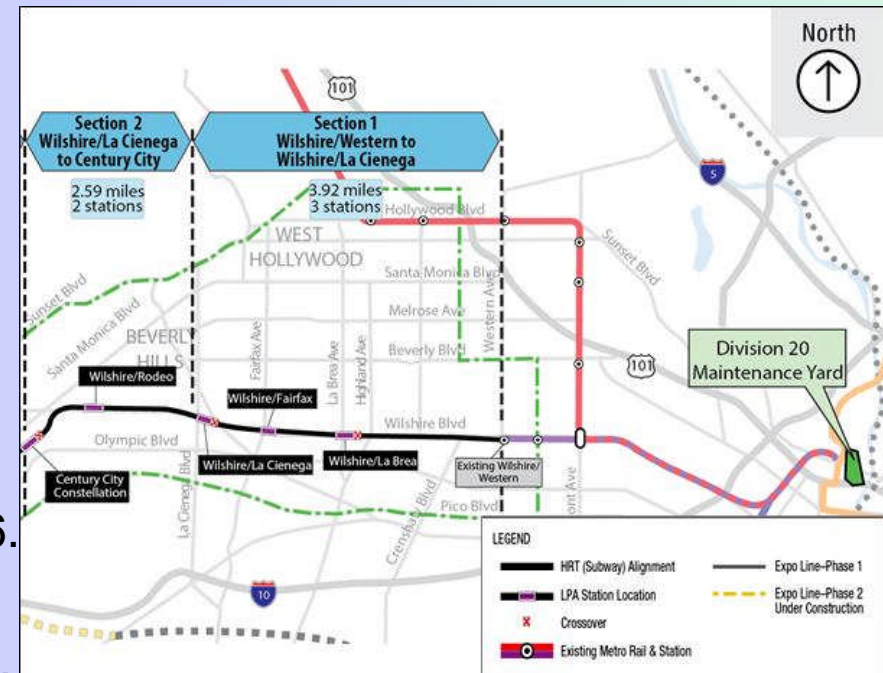

# I-405 SEPULVEDA PASS IMPROVEMENTS PROJECT

## SIGNIFICANT HIGHLIGHTS

- Contractor is working toward Final Completion
- Working through remaining items for final acceptance
- Preparation for Claim 86 arbitration is ongoing

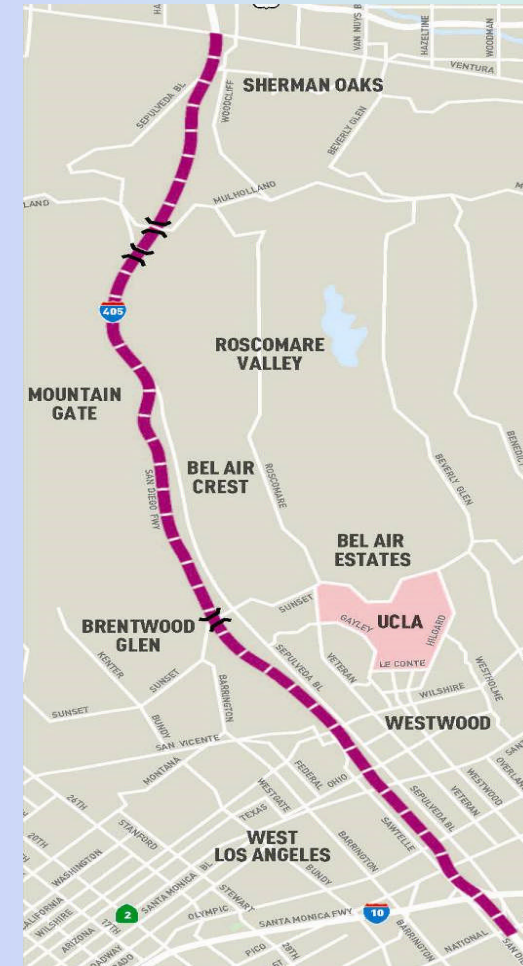

March 2016



Construction Committee  
Los Angeles County Metropolitan Transportation Authority



# GERALD DESMOND BRIDGE

## SIGNIFICANT HIGHLIGHTS

- Replacement of old, obsolete bridge to facilitate traffic to/from the Ports of Los Angeles/Long Beach
- Over 40% of international freight passes through the port complex
- Approximately \$1.4 Billion project; Metro share is \$17.3 Million
- Substantial Completion projected mid-2018

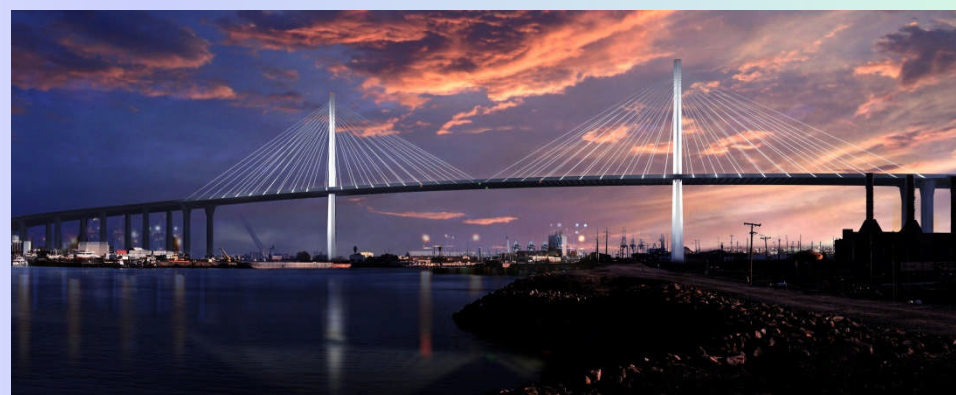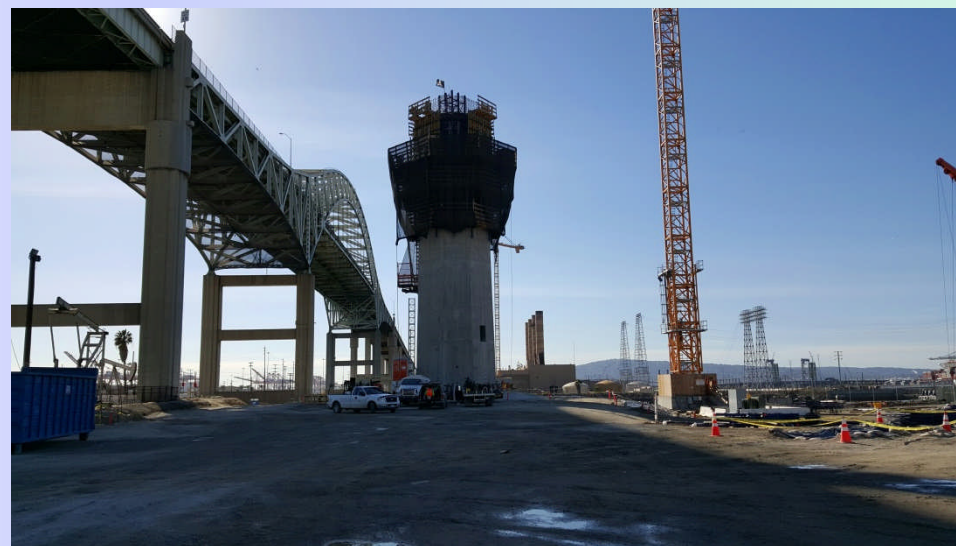

March 2016

**Construction Committee**  
Los Angeles County Metropolitan Transportation Authority








# DIVISION 13 BUS O&M FACILITY

## SIGNIFICANT HIGHLIGHTS

- Project is 100% complete and open as of February 1, 2016.
- Current activities work include completion of punch list, demobilization, and close out of the contract with McCarthy.
- Project has been selected as a finalist for Project of the Year by the LABJ Commercial Real Estate Awards

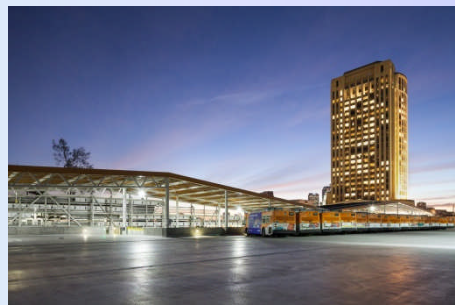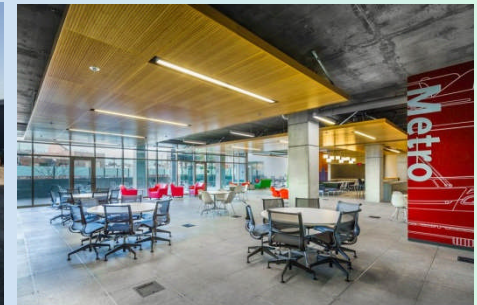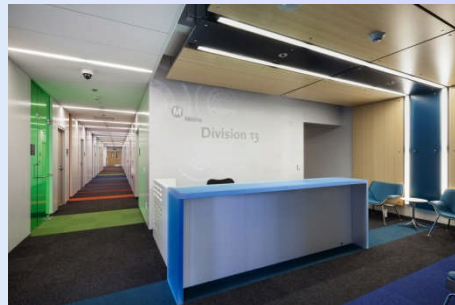

March 2016

Construction Committee  
Los Angeles County Metropolitan Transportation Authority



# PATSAOURAS PLAZA BUSWAY STATION

## SIGNIFICANT HIGHLIGHTS

- Construction start now scheduled for March/April 2016
- Work in progress includes approval of 100% design package with Caltrans, receipt of Caltrans permits, ROW certifications, utility clearances, resolution of environmental issues with Caltrans, exemptions to start construction, completion of final reports, and resolution of associated commercial issues with the Contractor.
- Board item for LOP budget increase on March 2016 agenda.
- Project completion scheduled for Summer 2017



March 2016

**Construction Committee**  
Los Angeles County Metropolitan Transportation Authority



# CIP PROJECTS

## MRL-MOL N. Hollywood Station West Entrance:

### Progress:

- Construction is 58% complete
- Targeted completion by June 2016
- Escalator installation ongoing
- Elevators installation to begin shortly
- Suspended slab work ongoing
- Electrical conduits installation ongoing
- Fire Protection piping installation ongoing



March 2016

Construction Committee  
Los Angeles County Metropolitan Transportation Authority



# CIP PROJECTS

## Universal Pedestrian Bridge:

### Progress:

- Construction 74% complete.
- Targeted completion by early April 2016 to coincide with opening of Harry Potter attraction
- Structural steel installation for bridge and Elevators is in progress
- Escalator installation at Station # 1 and # 3 is in progress
- Elevator installations at Station # 1, # 2, and # 3 scheduled to start shortly
- Transformer installation in progress
- Cost Risk: Shortfall in LOP Budget, staff on Board agenda for March 2016

























March 2016

Construction Committee  
Los Angeles County Metropolitan Transportation Authority



# Cost & Schedule Performance Summary Chart

| Project                                   | Cost Performance  | Schedule Performance  | Comments   |
|---|---|---|--|
| Crenshaw/LAX                              |    |    | The design-build contractor is currently reporting that they are behind schedule. Staff is working with contractor to attempt to mitigate delay.   |
| Westside Purple Line Extension-Section 1  |    |    |  |
| Regional Connector                        |    |    | LOP budget adjustment of \$131.8 million was approved by Metro Board in December. Project team is working with the DB contractor to develop a detailed recovery schedule to maintain FFGA RSD of May 29, 2021. The interface with city departments are critical to the success of the mitigation measures.                         |
| 1-405 Sepulveda Pass improvements Project |    |    | Final Acceptance is scheduled for March 16, 2016. Preparation for Claim 86 is ongoing.   |
| Universal City Pedestrian Bridge          |    |    | Construction is 75% complete and the schedule has been accelerated to substantially complete construction on April 6, 2016 to coincide with Universal's Harry Potter ride opening on April 7 <sup>th</sup> . Staff requesting LOP and CMA increases.   |
| MOL to MRL North Hollywood Connector      |    |    | Construction is 58% complete and is expected to substantially complete in June 2016. There are no significant issues on this project at this time.   |
| Patsaouras Plaza                          |    |    | Change orders have been negotiated for design error/tunnel conflict. Errors + Omissions process underway. Schedule delayed due to permitting, environmental, ROW issues with Caltrans, and resolution of associated commercial issues. Goal to start construction in March/April 2016. Board item to address budget in March 2016. |
| Division 13                               |  |  | Substantial completion occurred November 2, 2015, Certificate of Occupancy issued by LAFD December 3, 2015. Opened for revenue service February 1, 2016.   |
| P3010 Rail Car Vehicle Procurement        |  |  | First vehicles acceptance and vehicle level qualification testing are taking longer than planned. Kinkisharyo has informed Metro of potential delay to the delivery of 78 base order vehicles in 53 months. Though the delay will not impact the opening of any of Metro's new rail lines, mitigation plans are being developed.   |
| Gold Line Foothill Ext                    |  |  | Revenue operations scheduled to begin March 5, 2016  |
| Expo Phase II                             |  |  | Metro has accepted turnover of the Mainline and began Pre-Revenue Operations. Construction Authority is working to turn over the Yard Facility. Substantial Completion for the Expo Project will be achieved upon turnover of the Yard Facility. Operations and Maintenance Facility Turnover Application is under Metro review.   |



# ANNUAL PROGRAM EVALUATION (APE)

- Annual overall evaluation of Metro's capital program
- A detailed review of the project costs and schedule
- Reporting to the Board any differences in Life-of-Project budget and reasons for the changes
- A project management tool to bring greater consistency, transparency, and discipline
- Facilitates financial planning
