



Metro

Los Angeles County  
Metropolitan Transportation  
Authority  
One Gateway Plaza  
3rd Floor Board Room  
Los Angeles, CA

## Board Report

---

**File #:** 2016-0245, **File Type:** Informational Report

**Agenda Number:** 3.1

---

**REGULAR BOARD MEETING  
MARCH 24, 2016**

**SUBJECT: Foothill Gold Line Construction Authority Presentation**

PRESENTATION of resolution to the **Foothill Gold Line Construction Authority.**



# **Foothill Gold Line**

**Metro Board Meeting**

**March 24, 2016**


**9:00 am**

# March 5, 2016

## Foothill Gold Line Passenger Service Begins



# Foothill Gold Line Bridge

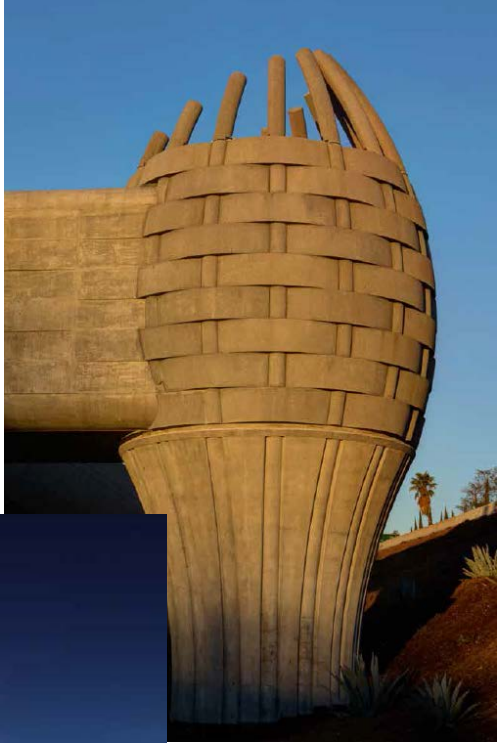



# Maintenance & Operations Facility





# Station Artwork





# Station Artwork



**ON TIME  
ON BUDGET**

**FOOTHILL GOLD LINE**



Foothill Gold Line



# Delivered On Time and On Budget



- Met Completion Date specified in light rail design-build contract
- All three design-build contracts completed within 10% of the original contract price value
- Completed within \$741 million funding agreement\*
  - \* Amended twice to meet new Metro contingency policies, add project features requested by Metro, and to accelerate project completion by two years

# Created Jobs During Great Recession

## Made Possible by Measure R

Initial  
Spending  
\$490 million

Employment  
6,900 jobs

Earnings  
\$308 million

Output  
\$930 million




Tax Revenue  
\$39 million





# Foothill Gold Line Future

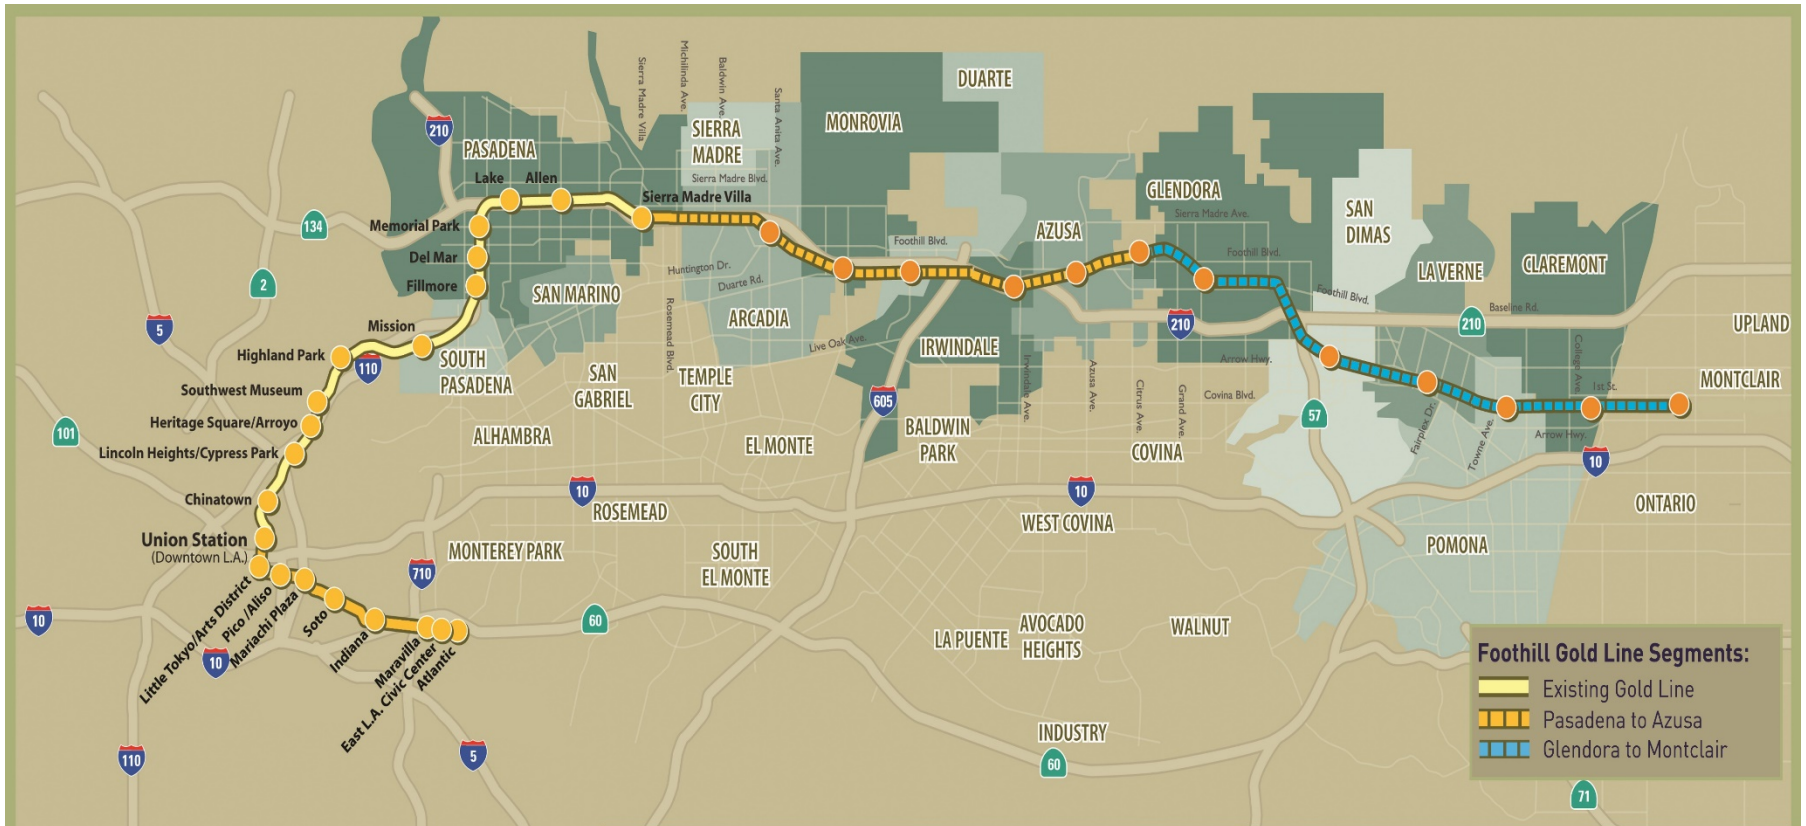

**Foothill Gold Line**

Connecting Los Angeles, the San Gabriel Valley and Inland Empire



**Foothill Gold Line**

# Making Glendora to Claremont Shovel Ready: 2017


- Launch two design-build procurements in 2017
- Third Party MOUs, approvals & project understanding , PUC approvals, Fire-life Safety MOU, Emergency Access Plan
- Advance conceptual engineering to refine project estimates and support third party reviews and approvals, PSR/PR
- Final Plan Set including major project elements, Geotechnical Reports, Traction Power Load Plan Study
- Prepare and ready draft design-build scope, contract terms and conditions
- Phase I & II Environmental Site Assessment Reports
- Project completion as early as late 2023





# Azusa to Montclair Work Plan Milestones

## Substantial Completion 2023-24

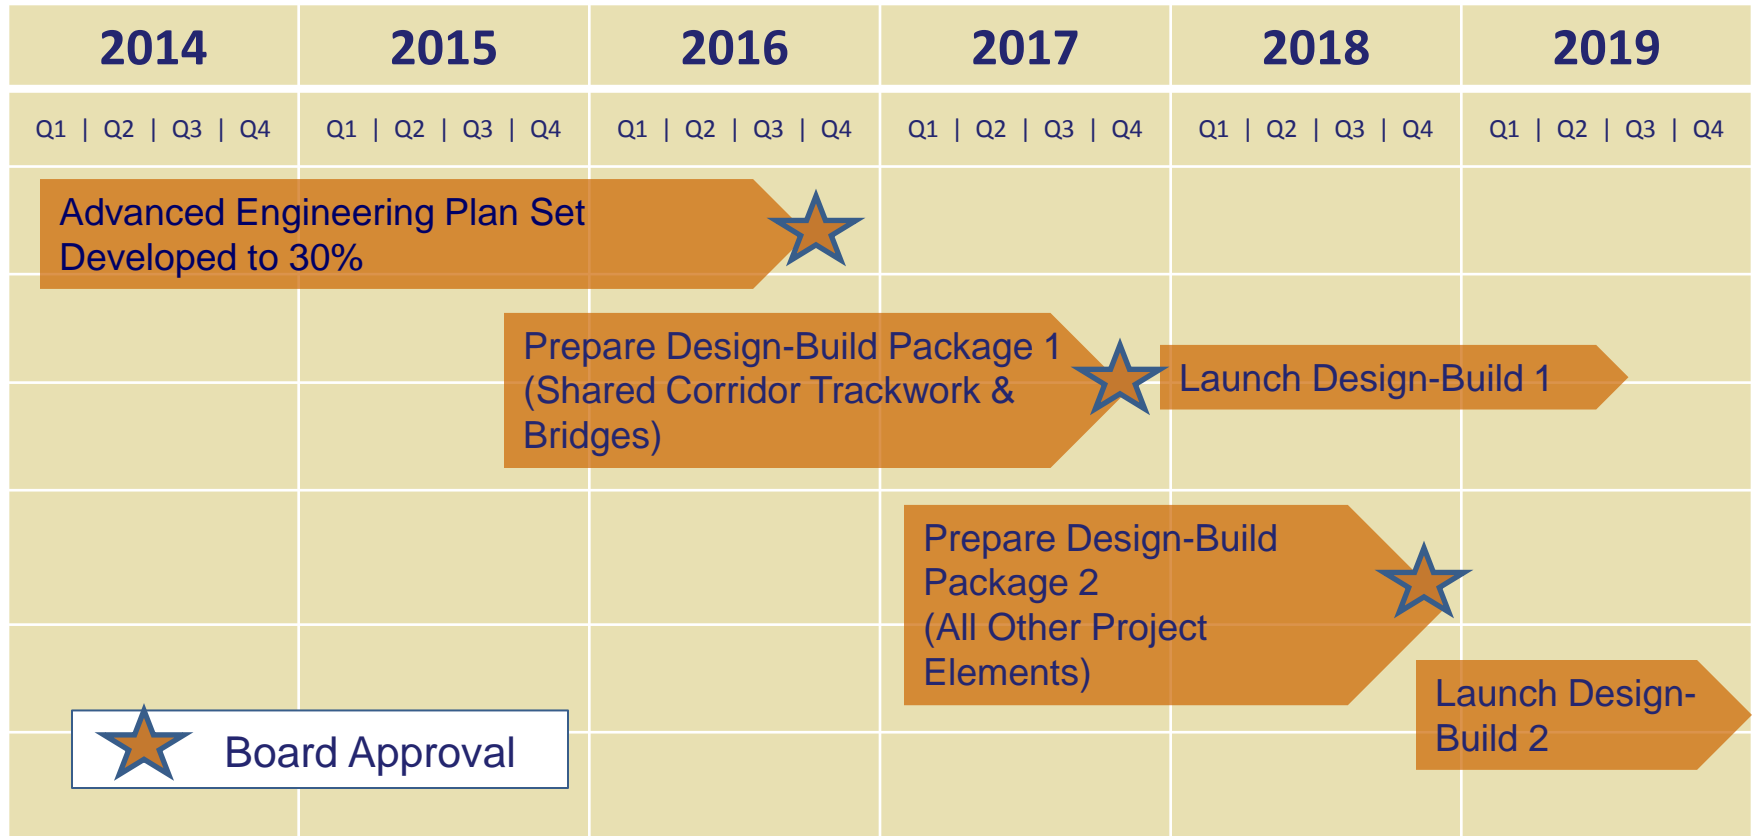

Schedule assumes construction funding available in 2017 if approved in proposed 2016 Los Angeles County Tax Measure



# FOOTHILL GOLD LINE

The Journey Continues



Foothill Gold Line



**Michael D. Antonovich**  
Los Angeles County Supervisor  
Fifth District

In observance of your leadership over this tour fulfilled

March 24, 2016

Foothill Gold Line Construction Authority  
Arcadia, Monrovia Duarte Irwindale Azusa

**The Journey Continues**



Foothill Gold Line
