

Metro

Los Angeles County
Metropolitan Transportation
Authority
One Gateway Plaza
3rd Floor Board Room
Los Angeles, CA



Metro

Board Report

File #: 2016-0295, **File Type:** Oral Report / Presentation

Agenda Number: 21.

**CONSTRUCTION COMMITTEE
APRIL 14, 2016**

RECEIVE Oral Report by the Caltrans District Director on Delivery of Projects on I-5.

Caltrans District 7 - Corridor Report for I-5 North Projects

April 2016 @ Metro Construction Committee by Shirley Choate, District 7 Chief Deputy




- Four projects, Segments 1-4, from SR 134 to SR 118, a total of ≈ 12 miles.
- Four lanes each direction. The freeway is being widened to add one HOV lane in each direction.
- Total I-5 North corridor budget is about \$886 million, \$501.6 million for Const Cap. Construction is within budget.
- All four segments are in the construction phase. **Segments 1 and 2 are substantially complete, the NB HOV lane opened March 2015 and the SB HOV lane opened May 27, 2015.**
- Empire IC Segment 3 and Southernmost Segment 4 HOV lane open-to-traffic target dates are for Winter 2018.
- Empire project has incentive provisions for the contractor to finish early.

North I-5 Corridor

Segment	EA	Phase	Phase % Complete	Description	Project Length/ Miles	Construction Award Amount	Contract Start Date	Open to Traffic
1	1219U	Const	99%	Add HOV from Route 170 to Route 118	3.4mi	\$121 M	5/06/2010A	2015
2	1218V	Const	99%	Add HOV lanes from Buena Vista Street to Route 170	4.4mi	\$59 M	10/14/2010A	2015
3	1218W	Const	40%	Empire Interchange from south of Magnolia Blvd. to just north of Buena Vista Street	2.2mi	\$196 M	12/20/2012A	Winter 2018*
4	12184	Const	67%	Add HOV lane from Route 134 to south of Magnolia Blvd.	2.7mi	\$58 M	12/6/2010A	Winter 2018 *
*These will be opened jointly								

Caltrans District 7 - Corridor Report for I-5 South Projects

April 2016 @ Metro Construction Committee by Shirley Choate, District 7 Chief Deputy

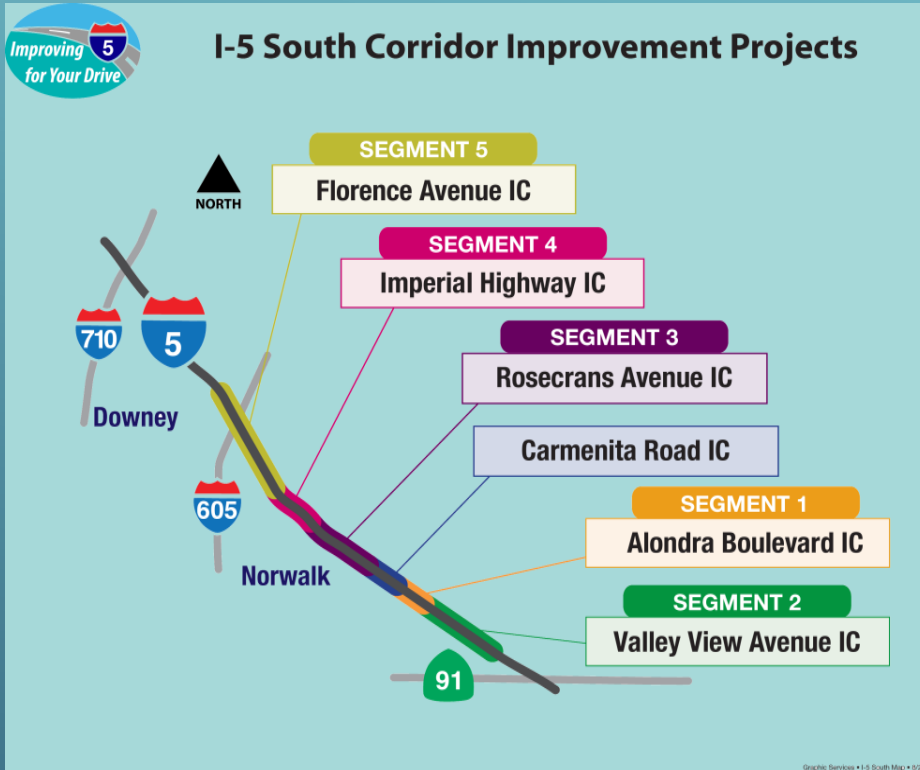

- Six projects including Carmenita Interchange and Segments 1 through 5, from OC County line to Interstate 605 and makes a total of approximately 7 miles.
- Three lanes in each direction. The freeway is being widened to add one general purpose lane and one HOV lane in each direction.
- The total I-5 South corridor budget is about \$1.88 billion with construction capital budget at \$674 million.
- 5 of 6 projects are in the construction phase, including Carmenita Interchange and Segments 1, 3, 4 and 5.
- **Segment 2 was advertised on March 7, 2016, bid opening on April 27, 2016.**
- **Ribbon-cutting for the entire Carmenita bridge, including all ramps, will be scheduled for Fall 2016.**

South I-5 Corridor

Segment	EA	Phase	Phase % Complete	Description	Project Length/Miles	Construction Award Amount	Contract Start Date	Open to Traffic
1	21591	Const	99%	Add HOV and mix flow lanes, Alondra Blvd. Interchange	0.9mi	\$45 M	12/21/2011A	Winter 2019
2	2159U	Const	0%	Add HOV and mix flow lanes, Valley View Ave. Interchange	1.4mi	N/A	Summer 2016	Winter 2019
3	21593	Const	71%	Widen and Realign Freeway, Rosecrans Ave. Interchange	1.3mi	89 M	9/18/2012A	Winter 2019
4	21594	Const	62%	Add HOV and mix flow lanes, Imperial Highway Interchange	1.8mi	\$142 M	9/18/2012A	Winter 2019
5	21595	Const	21%	Add HOV and mix flow lanes, Florence Ave. Interchange	1.7mi	\$96 M	5/13/2014A	Winter 2019
Carmenita	2159C	Const	84%	Carmenita Interchange	1.2mi	\$102 M	9/13/2011A	Winter 2019
