

Board Report

Los Angeles County
Metropolitan Transportation
Authority
One Gateway Plaza
3rd Floor Board Room
Los Angeles, CA

Agenda Number:

Attached is the official record distributed to the board.

AUGUST 12, 2022

TO: BOARD OF DIRECTORS

File #: 2022-0606, File Type: Board Correspondence

THROUGH: STEPHANIE WIGGINS

CHIEF EXECUTIVE OFFICER

FROM: JAMES DE LA LOZA

CHIEF PLANNING OFFICER

SUBJECT: MONTHLY MAJOR PROJECTS UPDATE - PLANNING

ISSUE

Countywide Planning and Development provides a monthly status report of the major planning efforts.

DISCUSSION

The attached report provides a summary of 14 projects in early and environmental stages of development, and activities since the last reporting. These include our four Pillar Projects and other transit corridor projects funded by Measure M. Some notable highlights include:

- Eastside Phase 2 The Draft EIR was released on June 30, 2022, kicking off a public review and comment period that is scheduled to end on August 29. This represents a 60-day comment period, while the minimum is typically 45 days as required by CEQA. Comments may be submitted online or by participating in scheduled public hearings, which will be held mostly in-person with one virtual session (see schedule in the attached presentation). As typical with Metro community engagement, all hearings will provide in-language services and accommodations meeting ADA requirements.
- Rail to River Active Transportation Corridor (Segment B) This month, through the Planning and Programming Committee (August 17, 2022), the Metro Board will receive findings from the Supplemental Alternatives Analysis and will take action on the staff recommendation to maintain Randolph Street as the preferred alignment.
- Vermont Transit Corridor The Metro Board also will receive a separate receive-and-file item
 with updates on the Community-Based Partnership Program and next steps for conducting
 environmental analysis for this corridor. This will be presented through the Planning and

Programming Committee in August.

• Rio Hondo Confluence Station Feasibility Study - This month, the Board will receive a Board Box memo presenting findings from the completed Feasibility Study.

NEXT STEPS

Metro staff continues to provide project-specific briefings (regularly scheduled and as-requested) to Board members and their staff. Metro staff and executive team will continue to work with the Board Chair to identify the frequency and method for providing future updates on Planning's major corridor projects.

Metro's Board has provided several directives in response to the state of Metro capital projects and industry trends driving cost. These have included establishing measures to manage and control project scope growth through all phases of project development, identifying and managing third party and utility requirements that contribute to project costs, and evaluating the Metro Rail System Design Criteria (Legistar 2022-0168).

Other efforts include the formation of a multi-departmental Early Intervention Team, and -- specific to Planning's monthly update report -- Director Dupont-Walker's Amendment directing staff to include cost estimate ranges and design levels for all projects (Legistar 2022-0361). As part of the Early Intervention Team, Planning staff is working with the Deputy CEO, Program Management and Operations to develop an agency-wide, consistent monitoring and reporting method on costs and design progress to support a broad program of cost-control strategies. Planning staff will begin to incorporate the requested information in future Monthly Major Projects Reports when available.



August 12, 2022

TO: BOARD OF DIRECTORS

THROUGH: STEPHANIE N. WIGGINS

CHIEF EXECUTIVE OFFICER

FROM: JAMES DE LA LOZA

CHIEF PLANNING OFFICER

SUBJECT: MONTHLY MAJOR PROJECTS UPDATE - PLANNING

ISSUE

Countywide Planning and Development provides a monthly status report of the major planning efforts.

DISCUSSION

The attached report provides a summary of 14 projects in early and environmental stages of development, and activities since the last reporting. These include our four Pillar Projects and other transit corridor projects funded by Measure M. Some notable highlights include:

- Eastside Phase 2 The Draft EIR was released on June 30, 2022, kicking off a public review and comment period that is scheduled to end on August 29. This represents a 60 day comment period, while the minimum is typically 45 days as required by CEQA. Comments may be submitted online or by participating in scheduled public hearings, which will be held mostly in-person with one virtual session (see schedule in the attached presentation). As typical with Metro community engagement, all hearings will provide inlanguage services and accommodations meeting ADA requirements.
- Rail to River Active Transportation Corridor (Segment B) This month, through the Planning and Programming Committee (August 17, 2022), the Metro Board will receive findings from the Supplemental Alternatives Analysis and will take action on the staff recommendation to maintain Randolph Street as the preferred alignment.

- Vermont Transit Corridor The Metro Board also will receive a separate receive-and-file item with updates on the Community-Based Partnership Program and next steps for conducting environmental analysis for this corridor. This will be presented through the Planning and Programming Committee in August.
- Rio Hondo Confluence Station Feasibility Study This month, the Board will receive a Board Box memo presenting findings from the completed Feasibility Study.

NEXT STEPS

Metro staff continues to provide project-specific briefings (regularly scheduled and as-requested) to Board members and their staff. Metro staff and executive team will continue to work with the Board Chair to identify the frequency and method for providing future updates on Planning's major corridor projects.

Metro's Board has provided several directives in response to the state of Metro capital projects and industry trends driving cost. These have included establishing measures to manage and control project scope growth through all phases of project development, identifying and managing third party and utility requirements that contribute to project costs, and evaluating the Metro Rail System Design Criteria (Legistar 2022-0168).

Other efforts include the formation of a multi-departmental Early Intervention Team, and -- specific to Planning's monthly update report -- Director Dupont-Walker's Amendment directing staff to include cost estimate ranges and design levels for all projects (Legistar 2022-0361). As part of the Early Intervention Team, Planning staff is working with the Deputy CEO, Program Management and Operations to develop an agency-wide, consistent monitoring and reporting method on costs and design progress to support a broad program of cost-control strategies. Planning staff will begin to incorporate the requested information in future Monthly Major Projects Reports when available.

Attachment: Status Update Report

Title 2

Countywide Planning Major Project Updates

August 2022 Update



> Major Pillar Projects


- A) West Santa Ana Branch
- B) Eastside Transit Corridor Phase 2
- C) Sepulveda Transit Corridor
- D) C (Green) Line Extension to Torrance

> Other Projects in Planning and Development

- Rail to River Active Transportation Corridor
- Vermont Transit Corridor
- Rio Hondo Confluence Station
- North Hollywood to Pasadena
- N. San Fernando Valley BRT
- Los Angeles River Path
- Crenshaw North Extension
- E. San Fernando Valley Shared ROW
- Centinela Grade Separation
- Arts District/6th Street Station




West Santa Ana Branch Transit Corridor




Recent Activities

- WSAB continues to meet with cities and key agencies/stakeholders such as Caltrans, CPUC and USACE to coordinate on Draft EIS/R comment responses and resolution
- July 2022: Received additional design and engineering comments from UPRR & Ports
- July/August 2022: Meeting(s) with Arts/Industrial District property owners for Slauson to LAUS Study

- Complete Design Input/Coordination by October 2022
- September 2022: Provide update on environmental, advanced engineering work (project risks, utilities investigations and mapping) and funding

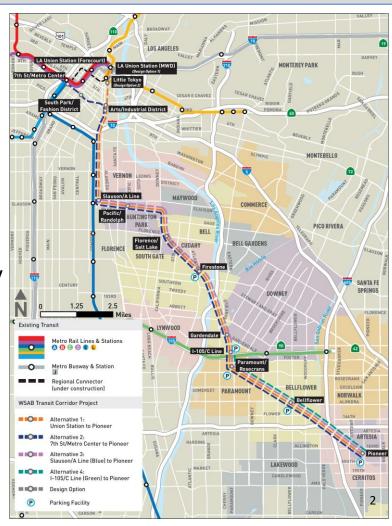


Eastside Transit Corridor Phase 2



Recent Activities

- Draft EIR released on June 30 (60-day comment period)
- Public Hearings
 - East LA (July 21)
 - Montebello (July 30)
 - Virtual (August 11)
 - Whittier (August 17)

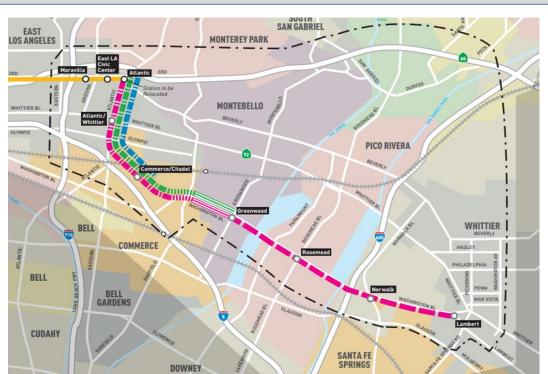

- Close of public review period on August 29, 2022
- Collaborating with Program Management on the advancement of engineering activities for alternate project delivery
- Return to Board with update on comments received and staff recommendation

Sepulveda Transit Corridor

Recent Activities


- June 15: Scoping Report released
- June 16: Virtual community meeting to review Scoping Report
- Ongoing engagement with third party agencies

- Prepare for fall community update meetings
- Continue to develop designs and prepare for environmental technical studies





C (Green) Line Extension to Torrance




Recent Activities

- Finalizing conceptual engineering plans and preparing environmental analysis
- Community meetings (open house)
 - Redondo Beach (August 11)
 - Virtual Meeting (August 15)
 - Torrance (August 16)
 - Lawndale (August 17)
- Ongoing meetings with cities, BNSF,
 Caltrans, utilities, and property owners


- Release Draft EIR: Winter 2022/23
- Board selection of Locally Preferred Alternative (LPA) in 2023



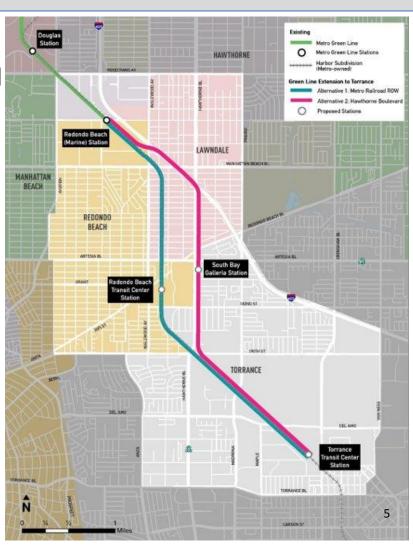

Rail to River Active Transportation Corridor

Segment B



Recent Activities

- August 2022: Metro Board Action
 - Receive findings of the Supplemental Alternatives Analysis
 - Receive and consider staff recommendation to maintain Randolph Street as preferred alignment




Next Actions

 Pending Board approval, continue coordinating recommended improvements with Corridor Cities and related projects in the area



Vermont Transit Corridor



Recent Activities

- August 2022: Return to Board with update on Community-Based Partnership Program (CPP) and proposed plan for environmental study
- Continued briefings for key stakeholders

- Develop environmental study scope informed by CPP feedback
- Initiate procurement for environmental study
- Coordinate with Service Planning on some potential near-term bus service improvements





Rio Hondo Confluence Station Feasibility Study



Recent Activities


- Completion of Feasibility Study
- August 2022: Present findings from Feasibility Study and provide staff recommendations (Board Box memo)

Next Actions

 Conduct briefings with Metro Board staff and key officials, as needed




North Hollywood to Pasadena BRT



Recent Activities


Preliminary
 engineering underway,
 including traffic
 analyses and
 preparation for
 First/Last Mile work

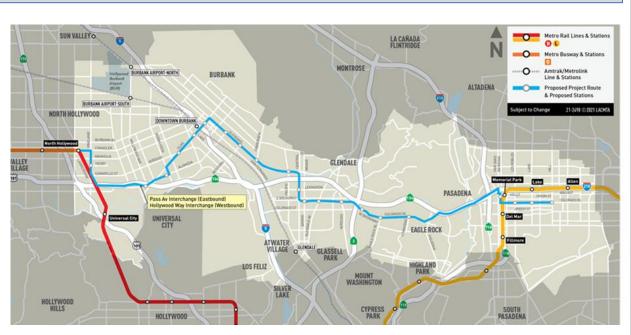

- Continue advancing design of bus lanes, station kit-of-parts, transit signal priority, and other project elements
- Continue coordinating with cities on project design in preparation for construction



North San Fernando Valley BRT Improvements



Recent Activities

- Continue key stakeholder engagement
- Community engagement and meetings in June
 - Virtual (June 15)
 - Panorama City (June 18)
 - CSUN (June 21)
 - Approximately 120 attendees
- Continue evaluation of proposed BRT Network Improvements in coordination with NextGen


Next Actions

 Anticipated Fall 2022 Board review of recommended BRT network improvements based on community input





Los Angeles River Path



Recent Activities


- Coordination meetings with stakeholders
 - Steering Committee meeting (June 27)
 - USACE Ecosystem Restoration (June 29)
 - LA River Cooperation Committee (July 11)
- Ongoing technical work for Draft EIR
- Ongoing advancement of bicycle/pedestrian bridge over US-101

- Project Development Team (PDT) Meeting
 Aug 24
- LA River Working Group Meeting Aug 30
- Public Meetings in September/October





Crenshaw Northern Extension



Recent Activities

- Public Outreach meetings on June 16 and June 21
 - 250 people attended/600 website visits
- Development of Storymap
- Continue to confirm project definition through Advanced Conceptual Engineering


Next Actions

 Initiate Travel Demand Forecasting & Environmental work on the Draft EIR





East San Fernando Valley Shared ROW Study



Recent Activities

- Deliverable status:
 - Data collection (completed)
 - Milestone 1 Grade Crossing Analysis (in progress)
- Study briefings with San Fernando City Council, Metro Board staff, and ESFV-area staff (LA Council Offices, City of LA)
- Technical meetings with City of San Fernando and Metrolink staff



- Complete grade crossing analysis and schematic layout of corridor
- Report back to the Metro Board, anticipated in Fall 2022
- Key stakeholder briefings and technical coordination as the study develops

Centinela Grade Separation

|-----|
Prelim Studies Environ Review 30% PE Design Pre-Con Award Constr Open

Recent Activities

- Design and utility coordination
 - City of Inglewood, CPUC, LA County (Public Works, Fire Dept., Sanitation Districts), SCE, SCG, AT&T, MCI Verizon, Lumen, Spectrum
- Construction coordination with Crenshaw/LAX project and Airport Metro Connector project

- Continue coordination with opening of Crenshaw/LAX pre-revenue testing and utility owners
- October 2022: Completion of 30% PE Design
- Fall 2022: Board review of Preliminary
 Engineering design, updated cost estimates, and project delivery alternative







Sample Rendering of Centinela Grade Separation (Source: HDR)

Arts District / 6th Street Station



Recent Activities

- Advancing conceptual station design, especially related to construction staging
- Developing ROM capital cost and ridership estimates

Next Actions

- Meeting with BNSF and Amtrak is critical to Draft EIR release
- Early Fall 2022 (anticipated): Draft EIR Release

Arts District/6th St Station Study Area





Measure M Expenditure Plan Groundbreaking to Opening Dates

